


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 169 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 51 different agencies and representing \$138 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right of way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

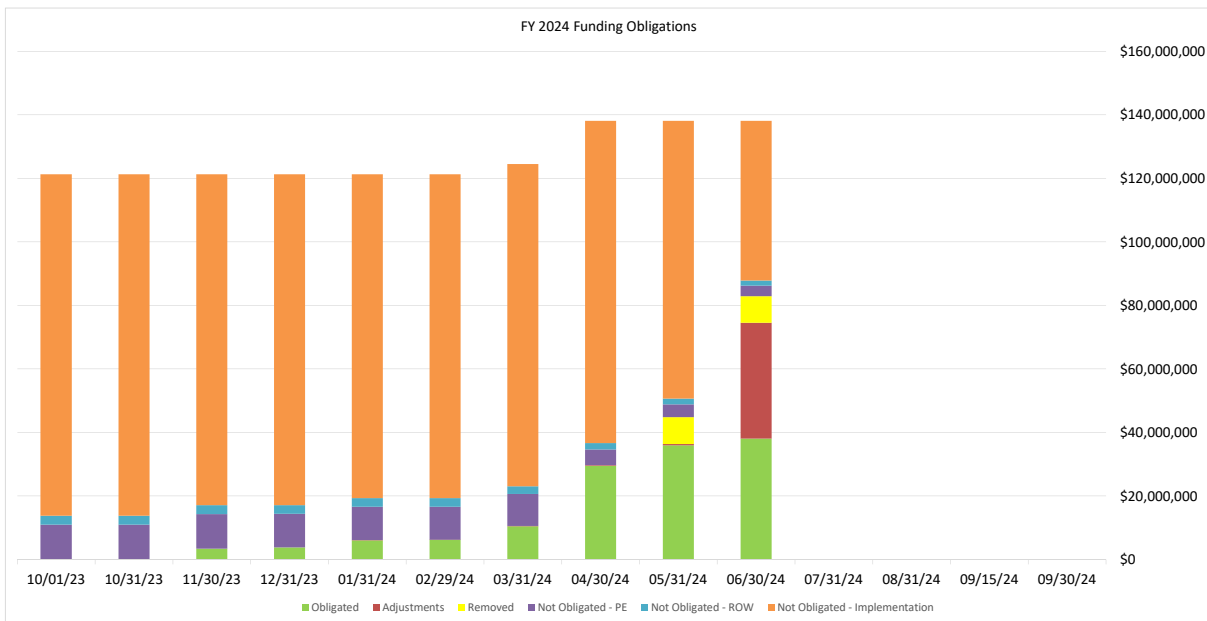

Date	Obligated		Adjustments		Removed		Not Obligated			Total Programmed				
	#	Federal \$	#	Federal \$	#	Federal \$	PE	ROW	CONST	#	Federal \$			
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
11/30/23	3	\$3,412,523	0	\$0	0	\$0	41	\$10,896,046	32	\$2,843,181	86	\$104,179,848	162	\$121,331,598
12/31/23	5	\$3,824,522	0	\$0	0	\$0	40	\$10,604,047	31	\$2,723,181	86	\$104,179,848	162	\$121,331,598
01/31/24	10	\$6,072,794	1	\$24,000	0	\$0	39	\$10,550,947	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
02/29/24	12	\$6,221,394	1	\$24,000	0	\$0	37	\$10,402,347	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
03/31/24	20	\$10,502,750	1	\$24,000	0	\$0	34	\$10,158,507	28	\$2,337,681	81	\$101,455,805	164	\$124,478,743
04/30/24	39	\$29,477,025	2	\$200,000	0	\$0	22	\$4,956,318	26	\$2,081,681	80	\$101,352,605	169	\$138,067,629
05/31/24	52	\$35,983,767	4	\$422,000	3	\$8,387,128	17	\$4,049,918	21	\$1,836,871	72	\$87,387,945	169	\$138,067,629
06/30/24	59	\$38,114,066	30	\$36,419,497	3	\$8,387,128	12	\$3,302,416	19	\$1,636,871	46	\$50,207,651	169	\$138,067,629
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds ROW - Right of Way Acquisition Funds CONST/IMPL - Construction Funds

Obligated						
Sponsor	Title - Description	TIP #	FY 2024 Federal	Phase	Scheduled Obligation	Actual Obligation
			TOTAL \$38,114,066	59 PROJECTS		
No Obligations in October						
October Total			\$0	0 Projects		
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24	11/06/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23	11/07/2023
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24	11/21/2023
November Total			\$3,412,523	3 Projects		
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24	12/15/2023
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23	12/28/2023
December Total			\$411,999	2 Projects		
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23	01/08/2024
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24	01/10/2024
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23	01/12/2024
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24	01/10/2024
O'Fallon	Egging Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23	01/16/2024
January Total			\$2,248,272	5 Projects		
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23	02/07/2024
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23	02/15/2024
February Total			\$148,600	2 Projects		
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23	03/07/2024
Des Peres	Des Peres Rd at Old Des Peres Rd - Roundabout	6976-20	\$1,047,855	CONST	Oct-24	03/11/2024
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24	03/11/2024
Jefferson County Port Authority	Marine Engine Repower - 2026 - Repower Two Tugboats Serving Mississippi River	7312-26	\$2,099,290	IMPL	Oct-24	03/29/2024
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24	03/07/2024
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23	03/19/2024
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24	03/07/2024
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24	03/29/2024
March Total			\$4,281,356	8 Projects		
Bi-State Development/ Metro	ADA Bus Stop Improvements - Bus Stop Improvements On 70 (Grand), 97 (Delmar, and 32 (MLK)	7325-25	\$2,400,000	IMPL	Oct-24	04/11/2024
Bi-State Development/ Metro	Bus Replacement - 2026 (A) - Replace 10 Buses	7286C-26	\$4,306,184	IMPL	Oct-25	04/11/2024
Bi-State Development/ Metro	Bus Replacement - 2026 (B) - Replace 10 Buses	7286D-26	\$4,306,184	IMPL	Oct-25	04/11/2024
Bi-State Development/ Metro	Call-A-Ride Van Replacement - 2027 (A) - Replace 9 Vans	7286A-27	\$1,288,259	IMPL	Oct-26	04/11/2024
Bi-State Development/ Metro	Call-A-Ride Van Replacement - 2027 (B) - Replace 9 Vans	7286B-27	\$1,288,259	IMPL	Oct-26	04/11/2024

Obligated						
Sponsor	Title - Description	TIP #	FY 2024 Federal	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$38,114,066			59 PROJECTS
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23	04/08/2024
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkrige Crossing To 150' N/O Hawkrige Trail Twtl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24	04/08/2024
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	IMPL	Jan-24	04/11/2024
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbahl Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trm Ln	7244B-24	\$340,000	PE	Oct-23	04/08/2024
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24	04/10/2024
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24	04/30/2024
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23	04/10/2024
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24	04/30/2024
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24	04/30/2024
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23	04/10/2024
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23	04/10/2024
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24	04/30/2024
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24	04/30/2024
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24	04/24/2024
April Total			\$18,974,275			19 Projects
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23	05/02/2024
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23	05/21/2024
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24	05/28/2024
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23	05/17/2024
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23	05/17/2024
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24	05/17/2024
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24	05/03/2024
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24	05/28/2024
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24	05/31/2024
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24	05/29/2024
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24	05/28/2024
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23	05/28/2024
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24	05/13/2024
May Total			\$6,506,742			13 Projects

Obligated						
Sponsor	Title - Description	TIP #	FY 2024 Federal	Phase	Scheduled Obligation	Actual Obligation
TOTAL			\$38,114,066			59 PROJECTS
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24	06/24/2024
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24	06/21/2024
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23	06/04/2024
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24	06/10/2024
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23	06/10/2024
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24	06/04/2024
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24	06/06/2024
June Total			\$2,130,299			7 Projects
July Total			\$0			0 Projects
August Total			\$0			0 Projects
September 15 Total			\$0			0 Projects
September 30 Total			\$0			0 Projects
Bold Indicates Project Received One-Time Extension						
Project Advanced From Future Year						

Not Obligated - Preliminary Engineering (PE)

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$3,302,416	12 PROJECTS	
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Mlk Drive - Hodiadmont Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24

Not Obligated - Right of Way (ROW)

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$1,636,871	19 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface - Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24

Not Obligated - Construction or Implementation (CONST or IMPL)					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$50,207,651	46 PROJECTS	
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	N. Main Street, Phase 2 - Valley Pl To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	IMPL	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbel Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24

Not Obligated - Construction or Implementation (CONST or IMPL)					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$50,207,651	46 PROJECTS	
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delpport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24
Bold Indicates Project Received One-Time Extension					

Adjustments							
Sponsor	Title - Description	TIP #	FY 2024	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$36,419,497	30 PROJECTS			
October Total				\$0	0 Projects		
November Total				\$0	0 Projects		
December Total				\$0	0 Projects		
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuivre River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24	Administrative Adjustment: Correction to Database Entry, ROW Programmed in FY 25 per application.	01/19/2024
January Total			\$24,000	1 Projects			
February Total				\$0	0 Projects		
March Total				\$0	0 Projects		
Jefferson County	Twin River Road - Byrnes Mill Rd/MO PP To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24	Project adjacent to Pleasant Valley Nature Reserve. 6(f) approval from Nat'l Park Service needed. Sponsor will use local funds for ROW acquisition.	04/22/2024
April Total			\$176,000	1 Projects			
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24	Floodplain/Regulatory Floodway and Section 106/Historic 4f approval needed. Sponsor will use local funds for ROW acquisition.	05/28/2024
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24	Sponsor will use local funds for preliminary plans.	05/31/2024
May Total			\$222,000	2 Projects			
Augusta	Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23	Board approved nine-month schedule ext.	06/26/2024
Clayton	Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24	Board approved nine-month schedule ext.	06/26/2024
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23	Board approved nine-month schedule ext.	06/26/2024
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24	Board approved nine-month schedule ext.	06/26/2024
Jefferson County	Dellwood Ln Resurfacing - Restripe For Twll - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24	EWG staff approved three-month schedule ext.	06/26/2024
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24	Sponsor will use local funds for ROW acquisition.	06/10/2024
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24	Sponsor will use local funds for ROW acquisition.	06/10/2024
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24	EWG staff approved three-month schedule ext.	06/26/2024
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24	Board approved nine-month schedule ext.	06/26/2024
Jefferson County	Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24	EWG staff approved three-month schedule ext.	06/26/2024
O'Fallon	Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24	Board approved nine-month schedule ext.	06/26/2024
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis	Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23	Board approved nine-month schedule ext.	06/26/2024
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis County	(Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis County	Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24	Board approved nine-month schedule ext.	06/26/2024
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24	Board approved nine-month schedule ext.	06/26/2024
University City	Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23	Board approved nine-month schedule ext.	06/26/2024
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24	Board approved nine-month schedule ext.	06/26/2024
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23	Board approved nine-month schedule ext.	06/26/2024
Wildwood	To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23	Board approved nine-month schedule ext.	06/26/2024
June Total			\$35,997,497	26 Projects			
July Total				\$0	0 Projects		
August Total				\$0	0 Projects		
September Total				\$0	0 Projects		

Removed							
Sponsor	Title - Description	TIP #	FY 2024	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$8,387,128	3 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
January Total			\$0	0 Projects			
February Total			\$0	0 Projects			
March Total			\$0	0 Projects			
April Total			\$0	0 Projects			
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24	Sponsor relinquished funds	05/31/2024
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24	Sponsor relinquished funds	05/31/2024
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	\$6,936,406	CONST	Jun-24	Sponsor relinquished funds	05/31/2024
May Total			\$8,387,128	3 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			
Bold Indicates Project Received One-Time Extension							


FY 2024 Reasonable Progress Update: May 31, 2024

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 169 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 51 different agencies and representing \$138 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right of way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

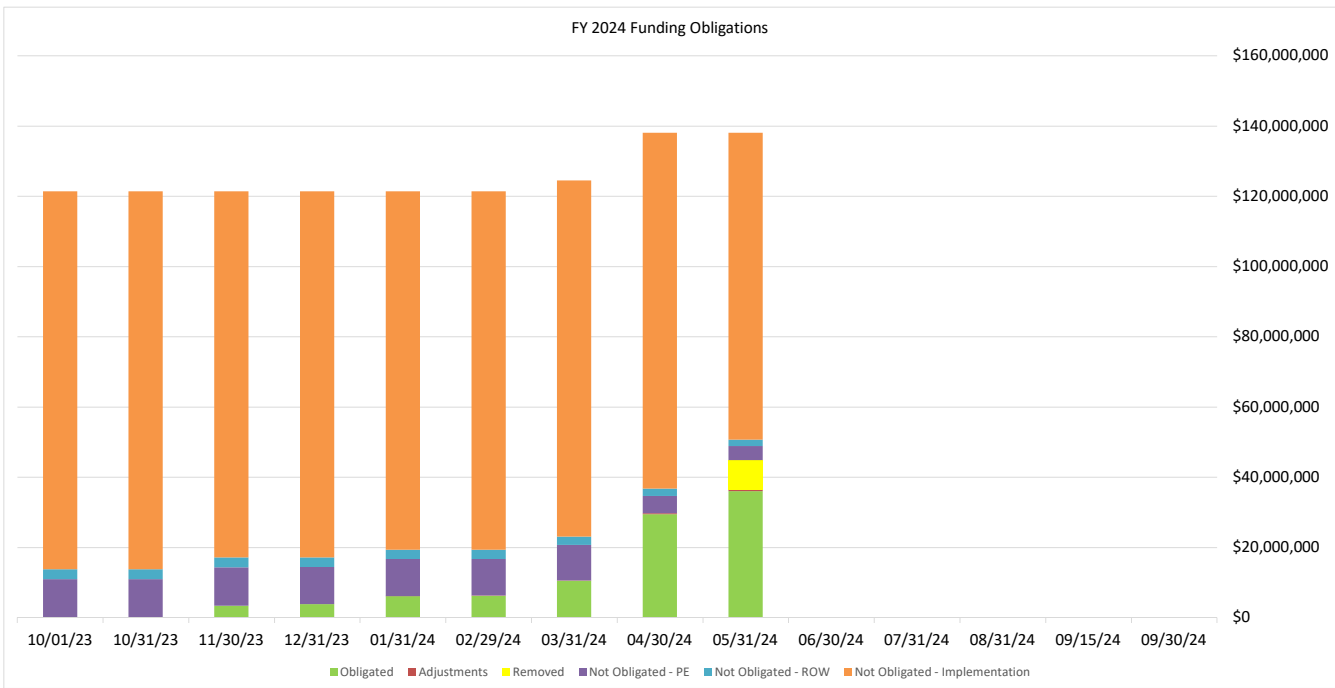

Date	Obligated		Adjustments		Removed		Not Obligated						Total Programmed	
	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$	#	Federal \$
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
11/30/23	3	\$3,412,523	0	\$0	0	\$0	41	\$10,896,046	32	\$2,843,181	86	\$104,179,848	162	\$121,331,598
12/31/23	5	\$3,824,522	0	\$0	0	\$0	40	\$10,604,047	31	\$2,723,181	86	\$104,179,848	162	\$121,331,598
01/31/24	10	\$6,072,794	1	\$24,000	0	\$0	39	\$10,550,947	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
02/29/24	12	\$6,221,394	1	\$24,000	0	\$0	37	\$10,402,347	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
03/31/24	20	\$10,502,750	1	\$24,000	0	\$0	34	\$10,158,507	28	\$2,337,681	81	\$101,455,805	164	\$124,478,743
04/30/24	39	\$29,477,025	2	\$200,000	0	\$0	22	\$4,956,318	26	\$2,081,681	80	\$101,352,605	169	\$138,067,629
05/31/24	52	\$35,983,767	4	\$422,000	3	\$8,387,128	17	\$4,049,918	21	\$1,836,871	72	\$87,387,945	169	\$138,067,629
06/30/24														
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2024 Federal	Phase	Scheduled Obligation	Actual Obligation
			TOTAL \$35,983,767	52 PROJECTS		
No Obligations in October						
October Total			\$0	0 Projects		
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24	11/06/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23	11/07/2023
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24	11/21/2023
November Total			\$3,412,523	3 Projects		
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24	12/15/2023
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23	12/28/2023
December Total			\$411,999	2 Projects		
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23	01/08/2024
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24	01/10/2024
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23	01/12/2024
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24	01/10/2024
O'Fallon	Egging Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23	01/16/2024
January Total			\$2,248,272	5 Projects		
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23	02/07/2024
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23	02/15/2024
February Total			\$148,600	2 Projects		
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23	03/07/2024
Des Peres	Des Peres Rd at Old Des Peres Rd - Roundabout	6976-20	\$1,047,855	CONST	Oct-24	03/11/2024
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24	03/11/2024
Jefferson County Port Authority	Marine Engine Repower - 2026 - Repower Two Tugboats Serving Mississippi River	7312-26	\$2,099,290	IMPL	Oct-24	03/29/2024
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24	03/07/2024
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23	03/19/2024
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24	03/07/2024
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24	03/29/2024
March Total			\$4,281,356	8 Projects		
Bi-State Development/ Metro	ADA Bus Stop Improvements - Bus Stop Improvements On 70 (Grand), 97 (Delmar, and 32 (MLK)	7325-25	\$2,400,000	IMPL	Oct-24	04/11/2024
Bi-State Development/ Metro	Bus Replacement - 2026 (A) - Replace 10 Buses	7286C-26	\$4,306,184	IMPL	Oct-25	04/11/2024
Bi-State Development/ Metro	Bus Replacement - 2026 (B) - Replace 10 Buses	7286D-26	\$4,306,184	IMPL	Oct-25	04/11/2024
Bi-State Development/ Metro	Call-A-Ride Van Replacement - 2027 (A) - Replace 9 Vans	7286A-27	\$1,288,259	IMPL	Oct-26	04/11/2024
Bi-State Development/ Metro	Call-A-Ride Van Replacement - 2027 (B) - Replace 9 Vans	7286B-27	\$1,288,259	IMPL	Oct-26	04/11/2024
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23	04/08/2024
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkrigde Crossing To 150' N/O Hawkrigde Trail Twtl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24	04/08/2024
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	IMPL	Jan-24	04/11/2024
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbehl Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trn Ln	7244B-24	\$340,000	PE	Oct-23	04/08/2024

Obligated						
Sponsor	Title - Description	TIP #	FY 2024 Federal	Phase	Scheduled Obligation	Actual Obligation
			TOTAL \$35,983,767	52 PROJECTS		
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24	04/10/2024
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24	04/30/2024
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23	04/10/2024
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24	04/30/2024
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24	04/30/2024
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23	04/10/2024
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23	04/10/2024
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24	04/30/2024
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24	04/30/2024
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24	04/24/2024
April Total			\$18,974,275	19 Projects		
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23	05/02/2024
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23	05/21/2024
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24	05/28/2024
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23	05/17/2024
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23	05/17/2024
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24	05/17/2024
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24	05/03/2024
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24	05/28/2024
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24	05/31/2024
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24	05/29/2024
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24	05/28/2024
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23	05/28/2024
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24	05/13/2024
May Total			\$6,506,742	13 Projects		
June Total			\$0	0 Projects		
July Total			\$0	0 Projects		
August Total			\$0	0 Projects		
September 15 Total			\$0	0 Projects		
September 30 Total			\$0	0 Projects		
Bold Indicates Project Received One-Time Extension						
Project Advanced From Future Year						

Adjustments							
Sponsor	Title - Description	TIP #	FY 2024	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$422,000	4 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuivre River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24	Administrative Adjustment: Correction to Database Entry, ROW Programmed in FY 25 per application.	01/19/2024
January Total			\$24,000	1 Projects			
February Total			\$0	0 Projects			
March Total			\$0	0 Projects			
Jefferson County	Twin River Road - Byrnes Mill Rd/MO PP To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24	Project adjacent to Pleasant Valley Nature Reserve. 6(f) approval from Nat'l Park Service needed. Sponsor will use local funds for ROW acquisition.	04/22/2024
April Total			\$176,000	1 Projects			
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24	Floodplain/Regulatory Floodway and Section 106/Historic 4f approval needed. Sponsor will use local funds for ROW acquisition.	05/28/2024
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24	Sponsor will use local funds for preliminary plans.	05/31/2024
May Total			\$222,000	2 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

Removed							
Sponsor	Title - Description	TIP #	FY 2024	Phase of Work	Scheduled Obligation	Reason for Removal	Removal Date
TOTAL			\$8,387,128		3 PROJECTS		
October Total			\$0		0 Projects		
November Total			\$0		0 Projects		
December Total			\$0		0 Projects		
January Total			\$0		0 Projects		
February Total			\$0		0 Projects		
March Total			\$0		0 Projects		
April Total			\$0		0 Projects		
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24	Sponsor relinquished funds	05/31/2024
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24	Sponsor relinquished funds	05/31/2024
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	\$6,936,406	CONST	Jun-24	Sponsor relinquished funds	05/31/2024
May Total			\$8,387,128		3 Projects		
June Total			\$0		0 Projects		
July Total			\$0		0 Projects		
August Total			\$0		0 Projects		
September Total			\$0		0 Projects		

Bold Indicates Project Received One-Time Extension

Not Obligated - Preliminary Engineering (PE)

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$4,049,918	17 PROJECTS	
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Milk Drive - Hodiament Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24

Not Obligated - Right of Way (ROW)

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$1,836,871	21	PROJECTS
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface -Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24

Not Obligated - Construction or Implementation (CONST or IMPL)					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$87,387,945	72 PROJECTS	
Augusta	Green, Walnut, Ferry, Chestnut Sidewalks - Green: Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Clayton	Brentwood/Central/Bemiston - Bw: Forsyth To Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	N. Main Street, Phase 2 - Valley Pl To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd To Dellwood Ln Resurfacing - Restripe For Twtl - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	IMPL	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbel Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24

Not Obligated - Construction or Implementation (CONST or IMPL)					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$87,387,945	72 PROJECTS	
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23
St. Louis	Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland PI Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24

Not Obligated - Construction or Implementation (CONST or IMPL)					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$87,387,945	72 PROJECTS	
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23

Bold Indicates Project Received One-Time Extension


FY 2024 Reasonable Progress Update: April 30, 2024

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council’s Policy on Reasonable Progress.

Currently, there are 169 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 51 different agencies and representing \$138 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a “one-time extension” of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

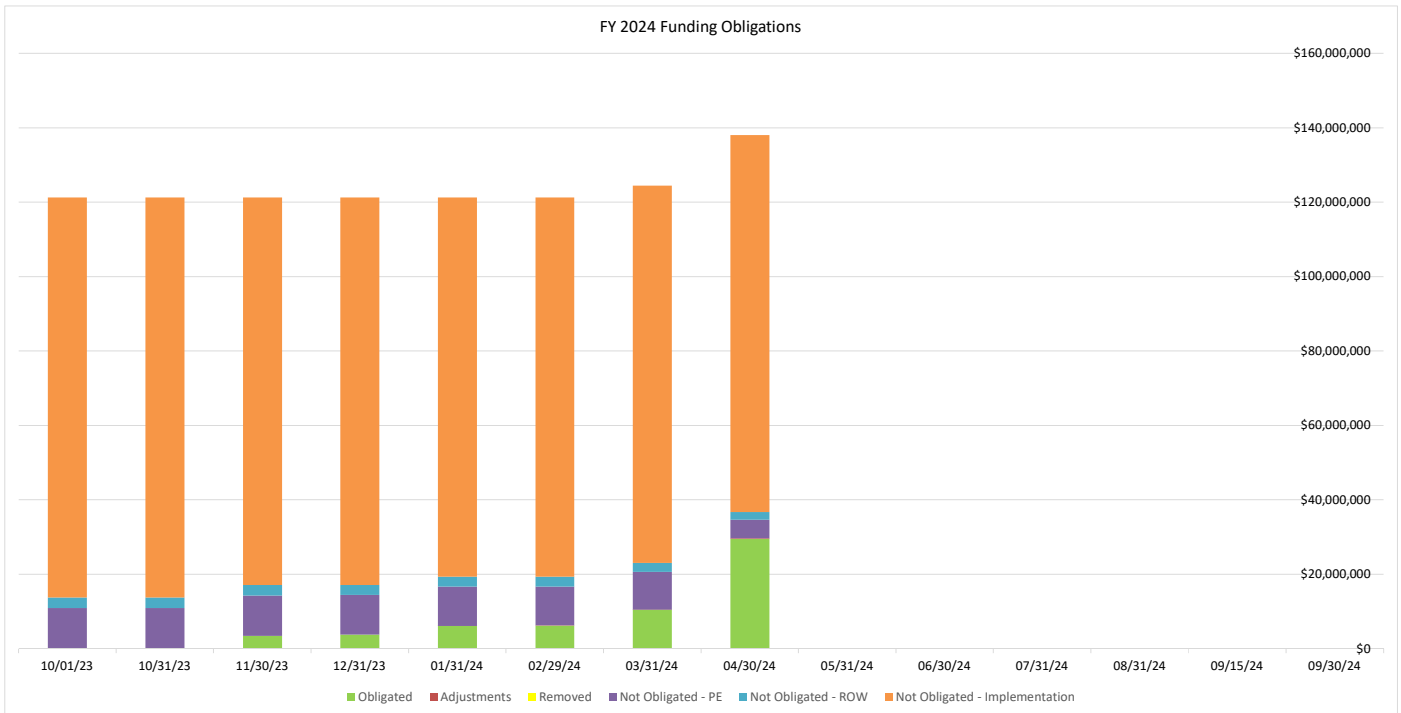

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	PE Federal \$	#	ROW Federal \$	#	CONST Federal \$	#	Federal \$
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
11/30/23	3	\$3,412,523	0	\$0	0	\$0	41	\$10,896,046	32	\$2,843,181	86	\$104,179,848	162	\$121,331,598
12/31/23	5	\$3,824,522	0	\$0	0	\$0	40	\$10,604,047	31	\$2,723,181	86	\$104,179,848	162	\$121,331,598
01/31/24	10	\$6,072,794	1	\$24,000	0	\$0	39	\$10,550,947	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
02/29/24	12	\$6,221,394	1	\$24,000	0	\$0	37	\$10,402,347	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
03/31/24	20	\$10,502,750	1	\$24,000	0	\$0	34	\$10,158,507	28	\$2,337,681	81	\$101,455,805	164	\$124,478,743
04/30/24	39	\$29,477,025	2	\$200,000	0	\$0	22	\$4,956,318	26	\$2,081,681	80	\$101,352,605	169	\$138,067,629
05/31/24														
06/30/24														
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$29,477,025		39 PROJECTS
			October Total		\$0	0 Projects
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24	11/06/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23	11/07/2023
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24	11/21/2023
			November Total		\$3,412,523	3 Projects
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24	12/15/2023
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23	12/28/2023
			December Total		\$411,999	2 Projects
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23	01/08/2024
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24	01/10/2024
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23	01/12/2024
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24	01/10/2024
O'Fallon	Egging Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23	01/16/2024
			January Total		\$2,248,272	5 Projects
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23	02/07/2024
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23	02/15/2024
			February Total		\$148,600	2 Projects
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23	03/07/2024
Des Peres	Des Peres Rd at Old Des Peres Rd - Roundabout	6976-20	\$1,047,855	CONST	Oct-24	03/11/2024
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24	03/11/2024
Jefferson County Port Authority	Marine Engine Repower - 2026 - Repower Two Tugboats Serving Mississippi River	7312-26	\$2,099,290	IMPL	Oct-24	03/29/2024
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24	03/07/2024
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23	03/19/2024
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24	03/07/2024
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24	03/29/2024
			March Total		\$4,281,356	8 Projects

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL \$29,477,025	39 PROJECTS		
Bi-State Development/Metro	ADA Bus Stop Improvements - Bus Stop Improvements On 70 (Grand), 97 (Delmar, and 32 (MLK)	7325-25	\$2,400,000	IMPL	Oct-24	04/11/2024
Bi-State Development/Metro	Bus Replacement - 2026 (A) - Replace 10 Buses	7286C-26	\$4,306,184	IMPL	Oct-25	04/11/2024
Bi-State Development/Metro	Bus Replacement - 2026 (B) -Replace 10 Buses	7286D-26	\$4,306,184	IMPL	Oct-25	04/11/2024
Bi-State Development/Metro	Call-A-Ride Van Replacement - 2027 (A) - Replace 9 Vans	7286A-27	\$1,288,259	IMPL	Oct-26	04/11/2024
Bi-State Development/Metro	Call-A-Ride Van Replacement - 2027 (B) - Replace 9 Vans	7286B-27	\$1,288,259	IMPL	Oct-26	04/11/2024
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23	04/08/2024
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkridge Crossing To 150' N/O Hawkridge Trail Twtl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24	04/08/2024
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	IMPL	Jan-24	04/11/2024
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbuhl Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trn Ln	7244B-24	\$340,000	PE	Oct-23	04/08/2024
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24	04/10/2024
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24	04/30/2024
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23	04/10/2024
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24	04/30/2024
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24	04/30/2024
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23	04/10/2024
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23	04/10/2024
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24	04/30/2024
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24	04/30/2024
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24	04/24/2024
			April Total	\$18,974,275	19 Projects	
			May Total	\$0	0 Projects	
			June Total	\$0	0 Projects	
			July Total	\$0	0 Projects	
			August Total	\$0	0 Projects	
			September 15 Total	\$0	0 Projects	
			September 30 Total	\$0	0 Projects	

Bold Indicates Project Received One-Time Extension

Project Advanced From Future Year

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$4,956,318	22 PROJECTS	
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Mlk Drive - Hodiamont Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$2,081,681	26 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface -Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$101,352,605	80 PROJECTS
Augusta	Green, Walnut, Ferry, Chestnut Sidewalks - Green: Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Clayton	Brentwood/Central/Bemiston - Bw: Forsyth To Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	N. Main Street, Phase 2 - Valley Pl To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd To Dellwood Ln Resurfacing - Restripe For Twtl - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$101,352,605	80 PROJECTS
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	IMPL	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbel Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$101,352,605	80	PROJECTS
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	\$6,936,406	CONST	Jun-24
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delpport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$200,000	2 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuivre River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24	Administrative Adjustment: Correction To Database Entry, ROW Programmed In FY 25 Per Application	01/19/2024
January Total			\$24,000	1 Projects			
February Total			\$0	0 Projects			
March Total			\$0	0 Projects			
Jefferson County	Twin River Road - Byrnes Mill Rd/MO PP To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24	Project adjacent to Pleasant Valley Nature Reserve 6(f) approval from Nat'l Park Service needed. Sponsor will use local funds for right of way acquisition.	\$45,404
April Total			\$176,000	1 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			


FY 2024 Reasonable Progress Update: March 31, 2024

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 164 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 50 different agencies and representing \$125 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

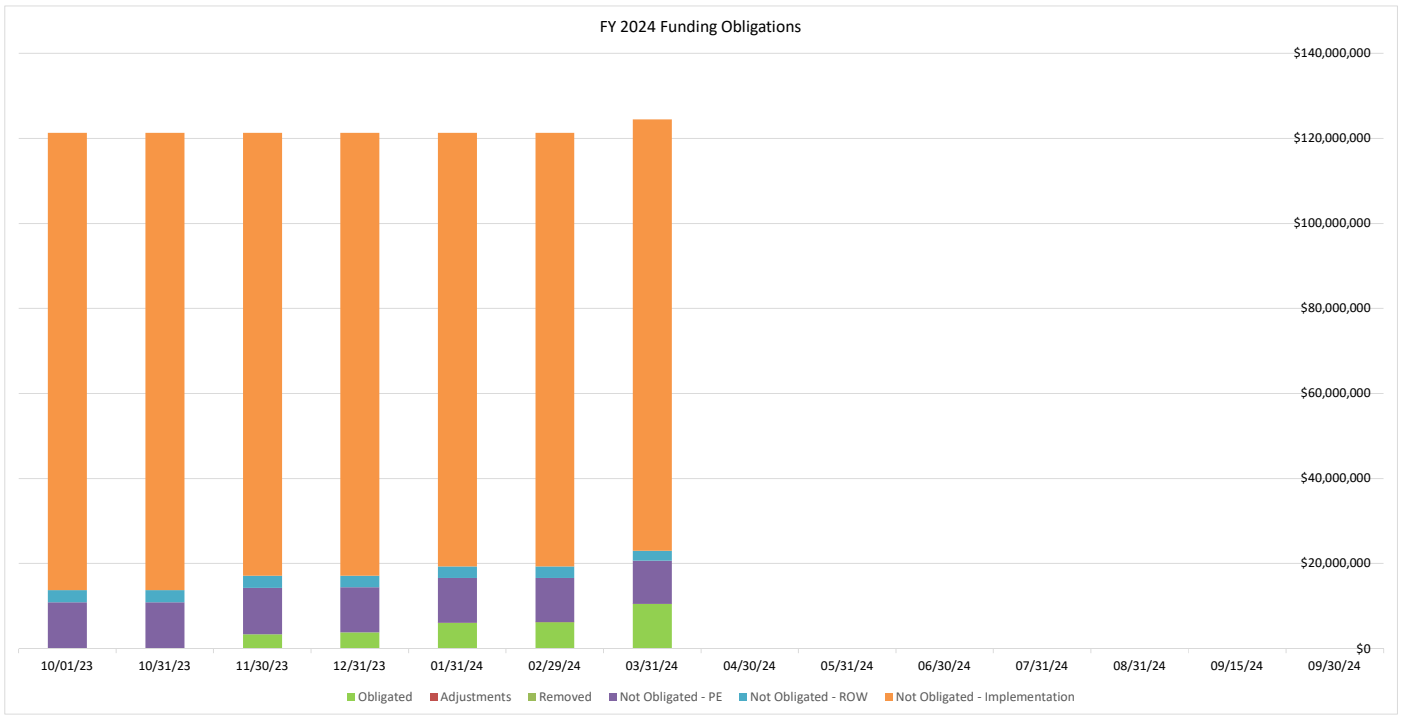

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	PE Federal \$	#	ROW Federal \$	#	CONST Federal \$	#	Federal \$
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
11/30/23	3	\$3,412,523	0	\$0	0	\$0	41	\$10,896,046	32	\$2,843,181	86	\$104,179,848	162	\$121,331,598
12/31/23	5	\$3,824,522	0	\$0	0	\$0	40	\$10,604,047	31	\$2,723,181	86	\$104,179,848	162	\$121,331,598
01/31/24	10	\$6,072,794	1	\$24,000	0	\$0	39	\$10,550,947	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
02/29/24	12	\$6,221,394	1	\$24,000	0	\$0	37	\$10,402,347	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
03/31/24	20	\$10,502,750	1	\$24,000	0	\$0	34	\$10,158,507	28	\$2,337,681	81	\$101,455,805	164	\$124,478,743
04/30/24														
05/31/24														
06/30/24														
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$10,502,750		20 PROJECTS
			October Total	\$0		0 Projects
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24	11/06/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23	11/07/2023
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24	11/21/2023
			November Total	\$3,412,523		3 Projects
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24	12/15/2023
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23	12/28/2023
			December Total	\$411,999		2 Projects
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23	01/08/2024
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24	01/10/2024
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23	01/12/2024
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24	01/10/2024
O'Fallon	Egginger Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23	01/16/2024
			January Total	\$2,248,272		5 Projects
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23	02/07/2024
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23	02/15/2024
			February Total	\$148,600		2 Projects
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23	03/07/2024
Des Peres	Des Peres Rd at Old Des Peres Rd - Roundabout	6976-20	\$1,047,855	CONST	Oct-24	03/11/2024
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24	03/11/2024
Jefferson County Port Authority	Marine Engine Repower - 2026 - Repower Two Tugboats Serving Mississippi River	7312-26	\$2,099,290	IMPL	Oct-24	03/29/2024
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24	03/07/2024
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23	03/19/2024
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24	03/07/2024
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24	03/29/2024
			March Total	\$4,281,356		8 Projects
			April Total	\$0		0 Projects
			May Total	\$0		0 Projects
			June Total	\$0		0 Projects
			July Total	\$0		0 Projects
			August Total	\$0		0 Projects
			September 15 Total	\$0		0 Projects
			September 30 Total	\$0		0 Projects

Bold Indicates Project Received One-Time Extension

Project Advanced From Future Year

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$10,158,507	34 PROJECTS	
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkridge Crossing To 150' N/O Hawkridge Trail Twtl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbel Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trn Ln	7244B-24	\$340,000	PE	Oct-23
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Mlk Drive - Hodiamont Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$10,158,507	34 PROJECTS	
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$2,337,681	28 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24
Jefferson County	Twin River Road - Byrnes Mill Rd/MO Pp To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface -Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$101,455,805	81	PROJECTS
Augusta	Green, Walnut, Ferry, Chestnut Sidewalks - Green: Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Clayton	Brentwood/Central/Bemiston - Bw: Forsyth To Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	N. Main Street, Phase 2 - Valley Pl To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd To Dellwood Ln Resurfacing - Restripe For Twtl - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$101,455,805	81 PROJECTS
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	CONST	Jan-24
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	CONST	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbel Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$101,455,805	81	PROJECTS
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	\$6,936,406	CONST	Jun-24
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delpport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$24,000		1 PROJECT		
October Total			\$0		0 Projects		
November Total			\$0		0 Projects		
December Total			\$0		0 Projects		
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuirve River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24	Administrative Adjustment: Correction To Database Entry, ROW Programmed In FY 25 Per Application	01/19/2024
January Total			\$24,000		1 Projects		
February Total			\$0		0 Projects		
March Total			\$0		0 Projects		
April Total			\$0		0 Projects		
May Total			\$0		0 Projects		
June Total			\$0		0 Projects		
July Total			\$0		0 Projects		
August Total			\$0		0 Projects		
September Total			\$0		0 Projects		

FY 2024 Reasonable Progress Update: February 29, 2024


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 162 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 49 different agencies and representing \$121 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2024 Funding Obligations

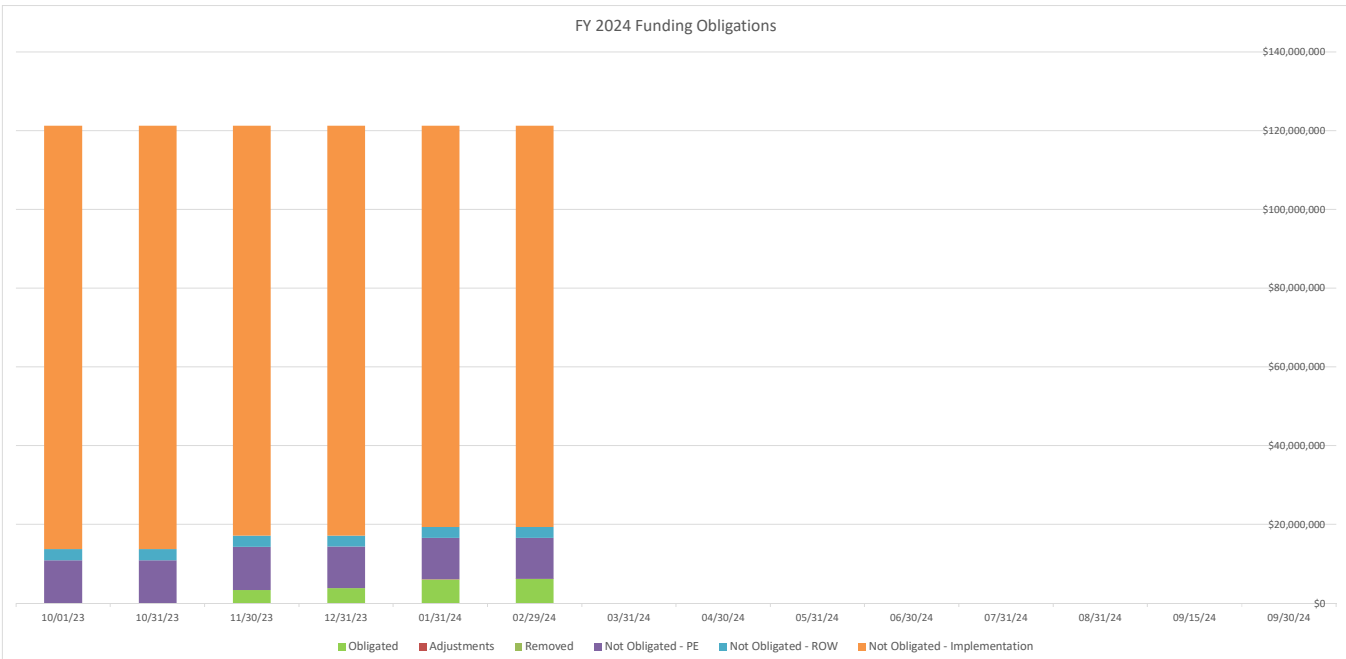

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	PE Federal \$	#	ROW Federal \$	#	CONST Federal \$	#	Federal \$
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
11/30/23	3	\$3,412,523	0	\$0	0	\$0	41	\$10,896,046	32	\$2,843,181	86	\$104,179,848	162	\$121,331,598
12/31/23	5	\$3,824,522	0	\$0	0	\$0	40	\$10,604,047	31	\$2,723,181	86	\$104,179,848	162	\$121,331,598
01/31/24	10	\$6,072,794	1	\$24,000	0	\$0	39	\$10,550,947	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
02/29/24	12	\$6,221,394	1	\$24,000	0	\$0	37	\$10,402,347	30	\$2,699,181	82	\$101,984,676	80	\$121,331,598
03/31/24														
04/30/24														
05/31/24														
06/30/24														
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$6,221,394	12 PROJECTS	
			October Total		\$0	0 Projects
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24	11/06/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23	11/07/2023
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24	11/21/2023
			November Total		\$3,412,523	3 Projects
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24	12/15/2023
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23	12/28/2023
			December Total		\$411,999	2 Projects
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23	01/08/2024
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24	01/10/2024
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23	01/12/2024
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24	01/10/2024
O'Fallon	Egging Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23	01/16/2024
			January Total		\$2,248,272	5 Projects
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23	02/07/2024
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23	02/15/2024
			February Total		\$148,600	2 Projects
			March Total		\$0	0 Projects
			April Total		\$0	0 Projects
			May Total		\$0	0 Projects
			June Total		\$0	0 Projects
			July Total		\$0	0 Projects
			August Total		\$0	0 Projects
			September 15 Total		\$0	0 Projects
			September 30 Total		\$0	0 Projects

Bold Indicates Project Received One-Time Extension

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$10,402,347	37 PROJECTS	
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkridge Crossing To 150' N/O Hawkridge Trail Twtl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbuhl Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trn Ln	7244B-24	\$340,000	PE	Oct-23
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Mlk Drive - Hodiamont Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$10,402,347	37 PROJECTS	
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$2,699,181	30 PROJECTS
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24
Jefferson County	Twin River Road - Byrnes Mill Rd/MO Pp To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface -Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$95,048,270	82 PROJECTS
Augusta	Green, Walnut, Ferry, Chestnut Sidewalks - Green: Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Clayton	Brentwood/Central/Bemiston - Bw: Forsyth To Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23
De Soto	N. Main Street, Phase 2 - Valley PI To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. Mcdonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd To Dellwood Ln Resurfacing - Restripe For Twtl - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$95,048,270	82 PROJECTS	
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	CONST	Jan-24
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	CONST	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbehl Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$95,048,270	82 PROJECTS	
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	7125A-23	CONST	Jun-24
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delpport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$95,048,270	82 PROJECTS	
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$24,000	1 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuivre River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24	ROW should have been scheduled in FY 2025 per original application	01/19/2024
January Total			\$24,000	1 Projects			
February Total			\$0	0 Projects			
March Total			\$0	0 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

FY 2024 Reasonable Progress Update: January 31, 2024


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 162 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 49 different agencies and representing \$121 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2024 Funding Obligations

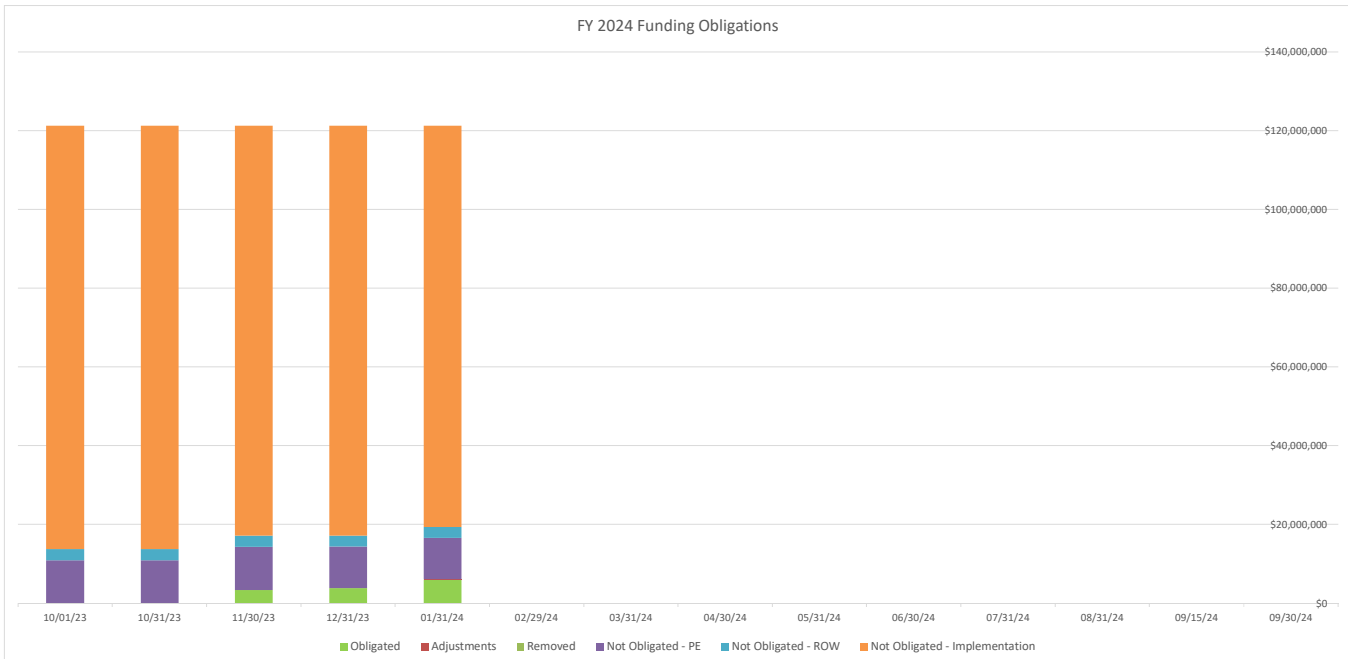

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	PE Federal \$	#	ROW Federal \$	#	CONST Federal \$	#	Federal \$
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
11/30/23	3	\$3,412,523	0	\$0	0	\$0	41	\$10,896,046	32	\$2,843,181	86	\$104,179,848	162	\$121,331,598
12/31/23	5	\$3,824,522	0	\$0	0	\$0	40	\$10,604,047	31	\$2,723,181	86	\$104,179,848	162	\$121,331,598
01/31/24	10	\$6,072,794	1	\$24,000	0	\$0	39	\$10,550,947	30	\$2,699,181	82	\$101,984,676	162	\$121,331,598
02/29/24														
03/31/24														
04/30/24														
05/31/24														
06/30/24														
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$6,072,794		10 PROJECTS
			October Total	\$0		0 Projects
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24	11/06/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23	11/07/2023
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24	11/21/2023
			November Total	\$3,412,523		3 Projects
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24	12/15/2023
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23	12/28/2023
			December Total	\$411,999		2 Projects
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23	01/08/2024
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24	01/10/2024
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23	01/12/2024
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24	01/10/2024
O'Fallon	Egging Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23	01/16/2024
			January Total	\$2,248,272		5 Projects
			February Total	\$0		0 Projects
			March Total	\$0		0 Projects
			April Total	\$0		0 Projects
			May Total	\$0		0 Projects
			June Total	\$0		0 Projects
			July Total	\$0		0 Projects
			August Total	\$0		0 Projects
			September 15 Total	\$0		0 Projects
			September 30 Total	\$0		0 Projects

Bold Indicates Project Received One-Time Extension

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$10,550,947	39 PROJECTS	
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkridge Crossing To 150' N/O Hawkridge Trail Twtl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbel Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trn Ln	7244B-24	\$340,000	PE	Oct-23
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Mlk Drive - Hodiamont Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$10,550,947	39 PROJECTS	
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$2,699,181	30 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24
Jefferson County	Twin River Road - Byrnes Mill Rd/MO Pp To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface -Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$101,984,676	82	PROJECTS
Augusta	Green, Walnut, Ferry, Chestnut Sidewalks - Green: Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Clayton	Brentwood/Central/Bemiston - Bw: Forsyth To Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23
De Soto	N. Main Street, Phase 2 - Valley PI To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd To Dellwood Ln Resurfacing - Restripe For Twtl - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$101,984,676	82 PROJECTS	
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	CONST	Jan-24
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	CONST	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbehl Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$101,984,676	82 PROJECTS
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	\$6,936,406	CONST	Jun-24
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delpport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$101,984,676	82 PROJECTS	
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23

Bold Indicates Project Received One-Time Extension

Adjustments							
Sponsor	Title - Description	TIP #	FY 2023	Phase of Work	Scheduled Obligation	Reason for Adjustment	Adjustment Date
TOTAL			\$24,000	1 PROJECTS			
October Total			\$0	0 Projects			
November Total			\$0	0 Projects			
December Total			\$0	0 Projects			
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuivre River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24	ROW should have been scheduled in FY 2025 per original application	01/19/2024
January Total			\$24,000	1 Projects			
February Total			\$0	0 Projects			
March Total			\$0	0 Projects			
April Total			\$0	0 Projects			
May Total			\$0	0 Projects			
June Total			\$0	0 Projects			
July Total			\$0	0 Projects			
August Total			\$0	0 Projects			
September Total			\$0	0 Projects			

FY 2024 Reasonable Progress Update: December 31, 2023


Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 162 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 49 different agencies and representing \$121 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2024 Funding Obligations

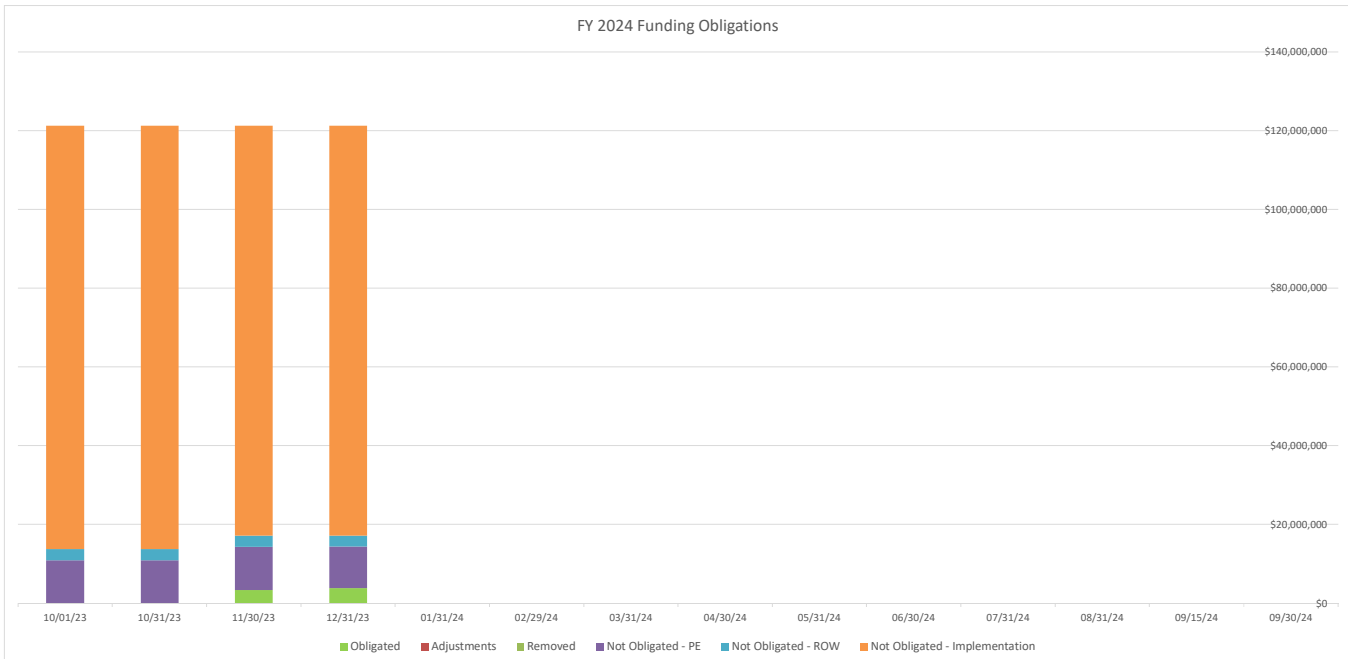

Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	PE Federal \$	#	ROW Federal \$	#	CONST Federal \$	#	Federal \$
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
11/30/23	3	\$3,412,523	0	\$0	0	\$0	41	\$10,896,046	32	\$2,843,181	86	\$104,179,848	162	\$121,331,598
12/31/23	5	\$3,824,522	0	\$0	0	\$0	40	\$10,604,047	31	\$2,723,181	86	\$104,179,848	162	\$121,331,598
01/31/24														
02/29/24														
03/31/24														
04/30/24														
05/31/24														
06/30/24														
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$3,824,522		5 PROJECTS
			October Total	\$0		0 Projects
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24	11/06/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23	11/07/2023
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24	11/21/2023
			November Total	\$3,412,523		3 Projects
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24	SL0184
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23	12/28/2023
			December Total	\$411,999		2 Projects
			January Total	\$0		0 Projects
			February Total	\$0		0 Projects
			March Total	\$0		0 Projects
			April Total	\$0		0 Projects
			May Total	\$0		0 Projects
			June Total	\$0		0 Projects
			July Total	\$0		0 Projects
			August Total	\$0		0 Projects
			September 15 Total	\$0		0 Projects
			September 30 Total	\$0		0 Projects

Bold Indicates Project Received One-Time Extension

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$10,604,047	40 PROJECTS
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkridge Crossing To 150' N/O Hawkridge Trail Twtl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
O'Fallon	Egginger Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbuhl Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trm Ln	7244B-24	\$340,000	PE	Oct-23
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Mlk Drive - Hodiamont Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$10,604,047	40 PROJECTS	
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$2,723,181	31 PROJECTS
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24
Jefferson County	Twin River Road - Byrnes Mill Rd/MO Pp To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface -Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuivre River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$104,179,848	86 PROJECTS
Augusta	Green, Walnut, Ferry, Chestnut Sidewalks - Green: Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Clayton	Brentwood/Central/Bemiston - Bw: Forsyth To Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23
De Soto	N. Main Street, Phase 2 - Valley Pl To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd To Dellwood Ln Resurfacing - Restripe For Twtl - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$104,179,848	86 PROJECTS
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	CONST	Jan-24
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	CONST	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbel Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$104,179,848	86 PROJECTS
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	\$6,936,406	CONST	Jun-24
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delpport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$104,179,848	86 PROJECTS	
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23

Bold Indicates Project Received One-Time Extension

FY 2024 Reasonable Progress Update: November 30, 2023

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 162 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 49 different agencies and representing \$121 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2024 Funding Obligations



Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	PE Federal \$	#	ROW Federal \$	#	CONST Federal \$	#	Federal \$
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
11/30/23	3	\$3,412,523	0	\$0	0	\$0	41	\$10,896,046	32	\$2,843,181	86	\$104,179,848	162	\$121,331,598
12/31/23														
01/31/24														
02/29/24														
03/31/24														
04/30/24														
05/31/24														
06/30/24														
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Obligated						
Sponsor	Title - Description	TIP #	FY 2023	Phase	Scheduled Obligation	Actual Obligation
			TOTAL	\$3,412,523		3 PROJECTS
			October Total	\$0		0 Projects
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24	11/06/2023
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23	11/07/2023
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24	11/21/2023
			November Total	\$3,412,523		3 Projects
			December Total	\$0		0 Projects
			January Total	\$0		0 Projects
			February Total	\$0		0 Projects
			March Total	\$0		0 Projects
			April Total	\$0		0 Projects
			May Total	\$0		0 Projects
			June Total	\$0		0 Projects
			July Total	\$0		0 Projects
			August Total	\$0		0 Projects
			September 15 Total	\$0		0 Projects
			September 30 Total	\$0		0 Projects

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$10,896,046	41 PROJECTS	
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkridge Crossing To 150' N/O Hawkridge Trail Twtl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
O'Fallon	Egginger Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbuhl Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trn Ln	7244B-24	\$340,000	PE	Oct-23
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Milk Drive - Hodiamont Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$10,896,046	41 PROJECTS	
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$2,843,181	32 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24
Jefferson County	Twin River Road - Byrnes Mill Rd/MO Pp To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface -Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuivre River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$104,179,848	86 PROJECTS
Augusta	Green, Walnut, Ferry, Chestnut Sidewalks - Green: Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Clayton	Brentwood/Central/Bemiston - Bw: Forsyth To Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23
De Soto	N. Main Street, Phase 2 - Valley Pl To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd To Dellwood Ln Resurfacing - Restripe For Twtl - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$104,179,848	86 PROJECTS
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	CONST	Jan-24
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	CONST	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbel Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandeventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$104,179,848	86 PROJECTS	
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	\$6,936,406	CONST	Jun-24
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delpport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$104,179,848	86 PROJECTS	
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23

Bold Indicates Project Received One-Time Extension

FY 2024 Reasonable Progress Update: October 31, 2023

Policy on Reasonable Progress

In the past, the lack of progress in developing and implementing projects using federal funds suballocated to the St. Louis region has led to significant project delays and created financial risks for both local and state transportation programs. Over the last several years, the East-West Gateway Council of Governments (EWGCOG) has taken a firm stance on delinquent projects through enforcement of the Council's Policy on Reasonable Progress.

Currently, there are 162 local projects in Missouri with federal funding programmed in Fiscal Year (FY) 2024 of the FY 2024-2027 Transportation Improvement Program (TIP). These projects, sponsored by 49 different agencies and representing \$121 million in federal funds, are subject to a September 30, 2024 deadline to obligate the federal funds, unless noted as receiving a schedule extension. To obligate funds, a sponsor must obtain approval from the Missouri Department of Transportation (MoDOT) for a specific milestone. Generally, a project must meet three milestones before construction or implementation of a project may begin: approval of design contract (PE), approval to acquire right-of-way (ROW), and final plan approval/authority to advertise (CONST/IMPL).

If a project is realizing delays that will put the federal funding at risk of forfeiture (i.e., not meet a September 30 deadline), the project sponsor will have the opportunity to request a "one-time extension" of their project schedule. The request for an extension is only available for projects with construction funds programmed in the current fiscal year and is due by June 1, 2024. One-time extensions of up to three (3) months may be granted by East-West Gateway staff and one-time extensions greater than three (3) months, but not more than nine (9) months, will go to the Board of Directors for their consideration and approval. If the project still cannot obligate funds after the one-time extension or the sponsor decides not to proceed, funding will be removed from the TIP, and the federal funds associated with those projects will be returned to the regional funding pool for redistribution without further action by the board.

FY 2024 Funding Obligations



Date	Obligated		Adjustments		Removed		Not Obligated						Total	
	#	Federal \$	#	Federal \$	#	Federal \$	#	PE Federal \$	#	ROW Federal \$	#	CONST Federal \$	#	Federal \$
10/01/23	0	\$0	0	\$0	0	\$0	42	\$10,948,046	32	\$2,843,181	88	\$107,540,371	162	\$121,331,598
10/31/23	0	\$0	0	\$0	0	\$0	42	\$10,948,084	32	\$2,843,181	88	\$107,540,371	162	\$121,331,636
11/30/23														
12/31/23														
01/31/24														
02/29/24														
03/31/24														
04/30/24														
05/31/24														
06/30/24														
07/31/24														
08/31/24														
09/15/24														
09/30/24														

PE - Preliminary Engineering Funds	ROW - Right of Way Acquisition Funds	CONST/IMPL - Construction Funds
------------------------------------	--------------------------------------	---------------------------------

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL \$10,948,046	42 PROJECTS	
Breckenridge Hills	Calvert Avenue Sidewalk - St. Charles Rock Rd To Baltimore Ave Sidewalk (5') - Lighting - Speed Humps	7269-24	\$52,000	PE	Apr-24
Charlack	Lackland Rd Bridge - East Of I-170 Bridge Deck Replacement	7287-24	\$44,000	PE	Feb-24
Chesterfield	Schoettler Road Sidewalk - Greenleaf Valley Dr To Windsor Valley Ct Sidewalk (5')	7270-24	\$91,000	PE	Nov-23
Crestwood	Rayburn/Samoa/Tahiti Sidewalk - Sappington Rd To Spellman Park Sidewalk (5')	7271-24	\$57,600	PE	Oct-23
Des Peres	Des Peres Road - Old Des Peres Rd To Dougherty Ferry Rd Resurfacing - Sidewalk Upgrades (5 Ft)	7290-24	\$183,324	PE	Mar-24
Ellisville	Pierside Lane - Old State Rd To Kiefer Creek Rd Resurfacing - Two-Way Bike Lane (8 Ft) - Curb Ramps	7292-24	\$87,840	PE	May-24
Florissant	St. Catherine Street - North New Florissant Road To Waterford Dr Resurfacing - Sup (10') - Sidewalk Upgrade (5') - Curb Ramps	7293-24	\$157,554	PE	Sep-24
Hazelwood	Teson Road - Howdershell Rd To Aubuchon Rd Resurfacing - Sidewalk(5') - Chatilion To Teson Garden	7239-24	\$163,750	PE	Jan-24
Kirkwood	Grant's Trail Extension, Phase 1 - Argonne To Leffingwell Ave Shared Use Path (10') - Intersection Improvements	7274-24	\$309,600	PE	Dec-23
Lake Saint Louis	Lake Saint Louis Blvd, Phase 2 - 200' S/O S Hawkridge Crossing To 150' N/O Hawkridge Trail Twl - Sup (10 Ft) - Sidewalk (6 Ft) - Reconstruct	7297-24	\$174,000	PE	Apr-24
Manchester	Carman Road Sidewalk - Labonne Pkwy To Dougherty Ferry Rd Sidewalk (5-6')	7275-24	\$136,000	PE	Dec-23
MoDOT	Traffic Monitoring Cameras - Add 155 CCTV Cameras To Cover Gaps In Existing Camera Network- Connect To Transportation Management Center	7314-24	\$291,999	PE	Sep-24
Northwoods	Natural Bridge (MO 115) Ped Lighting - Lucas And Hunt Rd To Avondale Rd Pedestrian Lighting	7298-24	\$24,000	PE	May-24
O'Fallon	Egginger Drive - St. Matthew Ave To Sonderen St Reconstruction - Upgrade Sidewalk (6')	7242A-24	\$53,100	PE	Oct-23
O'Fallon	Hoff Road, Phase 2 - Progress West Ln To City Limits (0.1 Mi. E/O Kemmar Ct) Reconstruct - Shared Use Path (10 Ft) - Realign Int.	7299A-24	\$150,000	PE	Mar-24
O'Fallon	Tom Ginnever - At N. Cool Springs Rd Roundabout - Shared Use Path (10 Ft)	7299B-24	\$85,800	PE	Mar-24
Shrewsbury	Weil Avenue - Laclede Station Rd To Wilshusen Ave Resurfacing - Sidewalk (5') - Curb/Gutter	7300-24	\$54,693	PE	Mar-24
St. Ann	Pear Tree Ln & Country Ln - Douglas Ct To City Limit Resurfacing - Sidewalk (4 Ft) - Curb Ramps	7301-24	\$56,000	PE	Sep-24
St. Charles	Fox Hill Rd - 490' S/O Boschertown Rd To N Randolph St Resurfacing - Sidewalk (5 Ft)	7302-24	\$80,000	PE	Sep-24
St. Charles	French Town Sidewalks - Decatur: 5th-2nd Morgan: 5th-2nd Olive: 5th-2nd Sidewalk (6') - Bike Climbing Ln	7278-24	\$105,000	PE	Dec-23
St. Charles	Regency Parkway - Veterans Memorial Pkwy To Zumbuhl Rd Reconstruct - Upgrade Sidewalks (5') - Two Way Trn Ln	7244B-24	\$340,000	PE	Oct-23
St. Charles County	County Wide Automated Traf. Signal Perf. Measures - Signal Optimization And Upgrad Signal Control Systems Along Various Routes	7303F-24	\$262,752	PE	Apr-24
St. Charles County	MO N - At Hopewell/Duello Rd New Traffic Signal - Shared Use Path (10')	7303H-24	\$160,000	PE	Apr-24
St. Louis	Grand Dr Bridge - Bridge Replacement - Shared Use Path (14 Ft) Buffered Bike Lanes (5 Ft)	7304B-24	\$584,000	PE	Apr-24
St. Louis	Loughborough Ave Bridge - Bridge Replacement - Shared Use Path (12 Ft) Sidewalk Upgrades (8 Ft) - Curb/Gutter	7304C-24	\$960,000	PE	Apr-24
St. Louis	Louisiana Avenue Calm Streets, Phase 2 - Meramec St To Holly Hills Ave Traffic Calming - Sidewalk -	7280-24	\$264,000	PE	Feb-24
St. Louis	Traffic Management Enhancements, Phase 6 - Dr. Milk Drive - Hodiadmont Ave To Grand Blvd Signal Control Upgrades - Traffic Cameras - Fiber	7304E-24	\$336,000	PE	Apr-24
St. Louis County	Airport Rd Multimodal Improvements - Hanley-Fay Dr: Sidewalks (5') Hanley- 360' W/O New Florissant-Protected Bike Lns	7281A-24	\$207,270	PE	Jul-24
St. Louis County	Chambers Road - 2027 - Bellefontaine Rd To City Limits E/O Grosvenor Dr Resurfacing - Sup (10') - Sidewalk Upgrades (5')	7305A-24	\$973,980	PE	Jan-24
St. Louis County	Hoffmeister Ave Sidewalks - Lemay Ferry Rd (MO 267) To Broadway (MO 231) Sidewalks (5')	7281B-24	\$197,600	PE	Dec-23
St. Louis County	Howdershell Road - 2027 - Lynn Haven Ln To Utz Rd Resurfacing - Sidewalks (5') - Flashing Yellow Arrows	7305B-24	\$1,141,720	PE	Jan-24

Not Obligated - Preliminary Engineering

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$10,948,046	42 PROJECTS	
St. Louis County	Lucas & Hunt Bridge - Over Norfolk & Southern RR -- Prelim Eng. Only Replace Southbound Bridge - Shared Use Path (12')	7305C-24	\$489,092	PE	Jan-24
St. Louis County	Mehl Ave Sidewalks - Old Halls Ferry Rd To New Halls Ferry Rd Sidewalks (5')	7281D-24	\$110,110	PE	Dec-23
St. Louis County	North & South Road Sidewalk - Olive Blvd (MO 340) To S/O Canton Ave Sidewalk (5')	7281C-24	\$80,240	PE	Dec-23
St. Louis County	Schuetz Road - 2027 - Gandy Dr To Lindbergh Blvd Resurfacing - Shared Use Path (10') - Curb Ramps	7305D-24	\$730,062	PE	Jan-24
St. Louis County	Vernon Ave - 2027 - Midland Ave To Westgate Ave Resurfacing - Shared Use Path (10') - Ln Reduction	7305E-24	\$697,796	PE	Jan-24
St. Paul	St. Paul Rd Bridge - Over Trib. To Peruque Creek Replace Bridge - Sidewalk (6 Ft)	7306-24	\$100,000	PE	Jan-24
St. Peters	Jungermann Rd, Phase 2 - McClay Rd To MoDOT ROW At MO 364 Resurfacing - Sidewalk Upgrades (6') - Curb/Gutter	7307-24	\$295,307	PE	Dec-23
St. Peters	Mid Rivers Mall Dr Shared Use Path - Former Rt N To MO 364 Shared Use Path (10')	7282-24	\$60,319	PE	Jan-24
Washington	MO 100 - At International Dr/Rabbit Trail Intersection Reconst - Right Turn Ln - Sidewalk (6')	7309B-24	\$224,064	PE	Dec-23
Washington	Third St - High St To Jefferson St Overlay - Sidewalk Upgrades (5 Ft) - Curb Ramps	7309A-24	\$175,474	PE	Sep-24
Webster Groves	Elm Avenue - Glendale Rd To Watson Rd (MO 366) Resurfacing - Shared Use Path (10') - Curb Ramps	7310-24	\$201,000	PE	May-24

Not Obligated - Right of Way					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$2,843,181	32 PROJECTS	
Arnold	Richardson Road - At Old Lemay Ferry Rd Intersection Realignment - Left Turn Lane	7231B-23	\$104,000	ROW	Jul-24
Creve Coeur	Craig Road - Olive Blvd (MO 340) To Old Ballas Rd Resurfacing - Sidewalks(6-8')	7176-24	\$80,000	ROW	Nov-23
Ferguson	Robert Avenue - N. Florissant Rd To N. Elizabeth Ave Reconstruct - Upgrade Sidewalks (5')	7179-23	\$44,000	ROW	Jan-24
Florissant	Mullanphy Road - Shackelford Rd to Patterson Rd - Resurfacing - Sidewalk (5') - Loveland to Vesper	7181-23	\$87,695	ROW	Oct-23
Glendale	Sappington Road - Manchester Rd (MO 100) To Lockwood Ave Resurfacing - Curb Ramps	7185-23	\$25,600	ROW	Oct-23
Jefferson County	Flucom Road - Hencher Rd To Athena School Rd Overlay - Shoulders (4') - Rumblestrips	7187A-23	\$60,000	ROW	Sep-24
Jefferson County	Harmony Hills Road Bridge - Over Pomme Creek Replace Bridge	7187B-23	\$80,000	ROW	Aug-24
Jefferson County	Market Street - Fourth St To Front St Reconstruction - Sidewalks(8') - Lighting	7187C-24	\$21,000	ROW	Sep-24
Jefferson County	Old Highway M - Glenstone Dr To Chasteen Ln Realignment - Shoulders (4') - Overlay - Rumble Strip	7187D-23	\$140,000	ROW	Aug-24
Jefferson County	Twin River Road - Byrnes Mill Rd/MO Pp To Osage Dr Overlay - Shoulders (4') - Rumble Strip	7187E-24	\$176,000	ROW	Sep-24
Kirkwood	S. Clay Avenue - Adams Ave To Woodbine Ave - Raised Intersections At Argonne/Jefferson Resurfacing - Upgr Sidewalks (5')	7188A-23	\$100,000	ROW	Oct-23
Kirkwood	S. Kirkwood Rd, Phase 2 - W. Monroe Ave To BNSF RR Resurfacing - Upgrade Sidewalks	7188B-23	\$100,000	ROW	Oct-23
Lake Saint Louis	South Lake Saint Louis Blvd, Phase 1 - Hawk Ridge Crossing To 300' S/O Hawk Ridge Circle Resurface -Twtl - Shared Use Path (10') - Sidewalk (5')	7235-23	\$35,000	ROW	Jun-24
Lake Saint Louis	Technology Drive - Lake Saint Louis Blvd To Technology Dr Loop Resurfacing - Sidewalk(6') - Shared Use Path (8')	7189-23	\$120,000	ROW	Dec-23
Manchester	Hanna Road - Hannafield Ct To Big Bend Rd Microsurfacing - Upgrade Sidewalks (5-6)	7190-24	\$96,000	ROW	Jan-24
Maplewood	Greenwood Boulevard - Sussex Ave To Canterbury Ave Reconstruction - Sidewalk (6-12')	7191-23	\$32,000	ROW	Oct-23
O'Fallon	Main Street, Phase 3 - St. Joseph Ave To RR Tracks (S/O Civic Dr) Resurfacing - Upgrade Sidewalks - Twtl	7192-23	\$116,000	ROW	Oct-23
St. Charles	Duchesne Drive - Droste Rd To W. Clay St Reconstruction - Lighting - Upgrade Sidewalks	7193A-23	\$360,000	ROW	Dec-23
St. Charles	Muegge Road - Mexico Rd To Old Muegge Rd Slab Replacement - Diamond Grind - Shared Use Path (10')	7193B-23	\$120,000	ROW	Dec-23
St. Charles County	Josephville Rd Bridge - Over Tributary Of Cuivre River Bridge Replacement	7303C-25	\$24,000	ROW	Sep-24
St. Louis	Lindell/Union Bridge - Over Forest Park Pkwy And Metrolink Bridge Replacement - Sidewalks	7123A-22	\$400,000	ROW	Nov-23
St. Louis	Traffic Management Enhancements, Phase 5 - Delmar: Debaliviere To Vandeventer Fiber - Sidewalk - Ptz Cameras - Interconnection	7246B-23	\$80,000	ROW	Jun-24
St. Louis County	Milburn Road - At Yaeger Rd Roundabout - Sidewalks	7247J-23	\$131,810	ROW	Sep-24
St. Peters	Barkwood Trails Drive - Jungermann Rd To Maple Tree Dr Reconstruction - Upgrade Sidewalk (6')	7197A-23	\$24,000	ROW	Dec-23
St. Peters	Harvester Road - At Queensbrooke Blvd - Replace Signal - Fiber Sidewalk - Queensbrooke To Sugarwood	7259-23	\$12,000	ROW	May-24
St. Peters	Jungs Station Road - Kings Crossing To Country Mill Ct Slab Replacement - Sidewalks (5') - Diamond Grind	7197B-23	\$32,000	ROW	Dec-23

Not Obligated - Right of Way

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
Sunset Hills	Rott Road/West Watson Road, Phase 2 - Robyn Rd To Weber Hill Rd Resurfacing - Sidewalk (5')	7248-23	\$120,000	ROW	Jun-24
University City	Pershing Avenue - Linden To Forest Park Pkwy - Linden To N Hanley Local Funds Resurfacing - Upgrade Sidewalks - Curb Ramps	7198-23	\$28,576	ROW	Oct-23
Washington	Front Street, Phase 2 - Stafford St To Jefferson St Resurfacing - Curb/Gutter - Upgrade Sidewalks	7199A-23	\$4,000	ROW	Jan-24
Washington	High Street, Phase 2 - Fifth St To Front St Resurfacing - Curb/Gutter - Upgrade Sidewalk	7199B-23	\$8,000	ROW	Dec-23
Wentzville	Mexico Road - Josephville Rd To Midland Park Dr Overlay - Shoulders (3') - Sidewalk (6') - Wwpark Dr To School	7200-23	\$80,000	ROW	Feb-24
Wentzville	Pearce Blvd - At Linn Ave Traffic Signal	7260-23	\$1,500	ROW	Jan-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$107,540,371	88 PROJECTS
Augusta	Green, Walnut, Ferry, Chestnut Sidewalks - Green: Locust-Walnut; Walnut: Jackson-Ferry Ferry: Locust-Chestnut; Chestnut: Jackson-Ferry	7153-24	\$226,027	CONST	Oct-23
Augusta	High/Jackson/Locust Sidewalk - High: Mt Pleasant Est. - Jackson: Jack: High-Locust Locust: Jackson - Church Rd; Sidewalks (5')	6937-22	\$481,788	CONST	Jun-24
Ballwin	Ries Road - Manchester Rd (MO 100) To Big Bend Rd Overlay - Curb Ramps - Lighting	7173-24	\$684,618	CONST	Dec-23
Clayton	Brentwood/Central/Bemiston - Bw: Forsyth To Maryland; Central: Maryland To Shaw Bemiston: Bonhomme To Maryland - Resurfacing	7175-24	\$800,000	CONST	Jun-24
Crestwood	Whitecliff Park Lane Bridge - Over Gravois Creek - Replace Bridge - Shared Use Path (8')	7105-22	\$1,069,212	CONST	Dec-23
Creve Coeur	US 67 - At Old Olive Street Rd Intersection Improvements - Bike/Ped Xing	7106-23	\$908,200	CONST	Oct-23
Crystal City	Taylor Ave - Connections To Mississippi Sidewalk - N/O 5Th To S/O 2Nd- Conn. To Mississippi At 2nd, 3rd, 4th, & 5th St Sidewalks (5')	7272-24	\$679,121	CONST	May-24
De Soto	Clarke Street - MO 21 To Main St Resurfacing	7177-24	\$528,871	CONST	Dec-23
De Soto	N. Main Street, Phase 2 - Valley Pl To Williams St Resurfacing - Sidewalk (6') - Lighting	7107-23	\$617,099	CONST	Jun-24
Dellwood	Hudson/Trask - Hudson: W. Florissant To Trask; Trask: Hudson To City Lim Overlay	7178-23	\$504,942	CONST	Dec-23
Des Peres	Lindemann Road - Manhattan Ave To Kirkwood City Limits (S/O Lillian Ave) Resurfacing - Sidewalk (6')	7108-22	\$259,416	CONST	Jan-24
Fenton	Old Highway 141 - Gravois Rd To County Line Resurfacing - Curb Ramps	7109-22	\$396,479	CONST	Oct-23
Festus	N. Mill Street - Main St To Cedar Heights Dr (City Limits) Resurfacing - Lighting	7180-24	\$708,708	CONST	Dec-23
Festus	W. Main Street, Phase 2 - Hancock Ct To Park Ave Resurfacing - Sidewalks (6') - Lighting	7110-23	\$470,065	CONST	Jun-24
Franklin County	Little Boone Creek Road Bridge - Over Little Boone Creek Replace Bridge - Shoulders (2')	7182A-24	\$635,914	CONST	Dec-23
Franklin County	MO 47 - At Union Expwy Roundabout	7125B-23	\$1,318,912	CONST	Jun-24
Frontenac	Geyer Road, Phase 2 - Hermitage Hill Rd Rd To Huntleigh Trails Ln Resurfacing - Sidewalk (6')	7112-22	\$2,061,120	CONST	Oct-23
Glendale	E. Essex Avenue - Sappington Rd To Dickson St Resurfacing - Sidewalk (5')	6949-21	\$634,777	CONST	Jun-24
Great Rivers Greenway	Brickline Greenway - Sarah St To Grand Ave Shared Use Path (12-14') - Bridge Over Vandeventer	7204-24	\$4,000,000	CONST	Jun-24
Great Rivers Greenway	Maline Greenway - Ted Jones Trail To W. Florissant Ave Shared Use Path (10') - Sidewalk (5')	6950-23	\$2,000,000	CONST	Jun-24
Hazelwood	Phantom Drive - Missouri Bottom Rd To James S. McDonnell Blvd Ln Reduction 4 To 2 Lns - Turn Lanes - Sidewalk (6')	6900-20	\$1,928,078	CONST	Jun-24
Jefferson County	Antire Road - 400' N/O Crestview Dr To 200' E/O Sunshine Dr Overlay - Shoulder (4') - Curve Impr. - Signage - Rumblestrip	7113D-22	\$917,000	CONST	Feb-24
Jefferson County	Dulin Creek Road - Meyer Ln To Local Hillsboro Rd Overlay - Shoulder (4') - Rumble Strips - Signage	7113E-23	\$732,386	CONST	Feb-24
Jefferson County	Gravois Road - 450' N/O Indian Springs Rd To Dellwood Ln Resurfacing - Restripe For Twtl - Shared Use Path (8')	7113A-23	\$962,500	CONST	Feb-24
Jefferson County	Hunning Road - Elizabeth Ln To Approx. 300' N/O Cinphany Ct Realign Curve - Shoulders (4') - Guardrail	6952B-21	\$784,800	CONST	Jun-24
Jefferson County	Old Lemay Ferry Rd, Phase 3 - Vogel Rd To Spring Forest Rd Reconstruction - Shoulders (5')	7113B-23	\$988,920	CONST	Feb-24
Jefferson County	Saline Road - Northwest Blvd To 400' S/O Memory Ln Overlay - Shoulders (4') - Rumble Strips - Signage	7113F-23	\$839,860	CONST	Feb-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
			TOTAL	\$107,540,371	88 PROJECTS
Kirkwood	Historic Amtrak Station Restoration - Restoration Of Train Station Const. In 1893 ADA Compliance - Exterior - Platform Cover	7158-22	\$1,382,812	CONST	Apr-24
Kirkwood	Kirkwood Road, Phase 1 - 100' S/O Swan Ave To Adams Ave Resurfacing - Upgrade Sidewalks	7114-22	\$1,091,126	CONST	Oct-23
Kirkwood	Lindemann Road - Dougherty Ferry Rd To Des Peres Limit (120' S/O MO ntour) Resurfacing - Upgrade Sidewalk (5') - Bike Lane (5')	7115-22	\$1,153,577	CONST	Oct-23
Kirkwood	W. Essex Avenue - Kirkwood Rd (US 61/67) To Geyer Rd Reconstruction - Replace Sidewalks (5') - Bike Ln	6953-22	\$1,304,000	CONST	Jun-24
Lake Saint Louis	Lake Saint Louis Blvd Uptown Sidewalk - S/O Veterans Memorial Pkwy To Spillway Bridge Sidewalks (6')	7159-22	\$643,723	CONST	Jan-24
Madison County Transit District	Ridefinders Marketing & Outreach - 2024 - MO - Increase Awareness, Interest, And Participation In Ridefinders By Employers And Commuters	7313A-24	\$1,600,000	CONST	Jan-24
Madison County Transit District	Ridefinders Vanpool Fleet Acquisition - 2024 - MO - Van Replacement	7313B-24	\$103,200	CONST	Jan-24
Manchester	Manchester Rd (MO 100) Sidewalk - Baxter Rd To MO 141 Sidewalks (5-6') - Ped Bridge	7117-22	\$671,700	CONST	Jun-24
MoDOT	Natural Bridge (MO 115) Sidewalks - Dardenne Ave To Avondale Ave Sidewalks (5') - Lighting - Mid Block Xings	7119-22	\$999,400	CONST	Oct-23
MoDOT	Signal Optimization - 2024 - MO 141: I-64 To Gravois Bluffs	7208-24	\$1,104,240	CONST	Jan-24
O'Fallon	Dardenne Greenway Connection - Phoenix Pkwy To Barat Haven Blvd Shared Use Path (10') - Parking Lot (Locally Funded)	7161-22	\$572,188	CONST	Feb-24
O'Fallon	Main Street, Phase 2 - Pitman St To Terra Rd Resurfacing - Shared Use Path (8') - Upgrade Sidewalk (5')	7118-22	\$1,207,393	CONST	Jun-24
O'Fallon	MO N - At MO K Add Dual Left Turn Lanes	7242B-24	\$904,761	CONST	Mar-24
O'Fallon	Weldon Spring Road, Phase 1 - Technology Dr To Valleybrook Dr Roundabout-Two Way Turn Ln - Reconstruct (Local Funds)	7209-22	\$920,440	CONST	Feb-24
Pacific	Osage St - At First Street Add Right Turn Lane - Intersection Improvements	7210-22	\$683,693	CONST	Feb-24
Pacific	Union Street Sidewalk - Sanker St To Neosho St Sidewalks (5')	7277-24	\$955,664	CONST	May-24
St. Charles	Hawks Nest Drive - W. Clay St To Zumbel Rd Reconstruction - Slab Repl. - Sup (10') - Sidewalk (5')	7121-24	\$2,000,000	CONST	Oct-23
St. Charles	S. Fifth Street - Fairgrounds Rd To San Juan Dr Reconstruction - Sidewalk (5') - Shared Use Path (10')	6960-23	\$1,500,000	CONST	Jun-24
St. Charles	Second Street - First Capitol Dr To Boones Lick Rd Reconstruction - Upgrade Sidewalks (5')	7120-22	\$1,720,000	CONST	Mar-24
St. Charles	Sibley Street/Lindenwood Avenue Sidewalk - Sibley: Duchesne - Lindenwood; Lindenwood: Alley- Elm Sidewalk (5-6')	7164-22	\$536,000	CONST	Feb-24
St. Charles County	Augusta Bottom Road Bridge - Over Tributary Of Missouri River Replace Bridge - Shoulders (4')	7194A-24	\$480,000	CONST	Nov-23
St. Charles County	Dardenne Prairie Signal Interconnect - Along Feise Rd, Town Square Ave And Hanley Rd Fiber Interconnection - Upgrade Traffic Controllers	7203-22	\$336,282	CONST	Oct-23
St. Charles County	Duello Road, Phase 3A - MO N to Orf Rd - Reconstruction - Sidewalks (5') - Turn Lanes	7122A-23	\$1,100,000	CONST	Dec-23
St. Charles County	Femme Osage Creek Road Bridge - Over Tributary Of Femme Osage Creek Replace Bridge - Shoulders (4')	7194B-24	\$504,000	CONST	Nov-23
St. Charles County	GGL - Mexico Rd Signal Performance Module - Bryan Rd To Cave Springs Rd Automated Traffic Signal Perf. - Signal Optimization	7211A-22	\$2,260,523	CONST	Mar-24
St. Charles County	Main Street (O'Fallon) ATSPM - MO P To Pitman St Signal Optimization	7258B-23	\$373,541	CONST	Mar-24
St. Louis	Columbia And Southwest Bridge - Over Union Pacific Railroad Replace Southwest Bridge - Realign Columbia To Southwest	6502B-22	\$6,320,000	CONST	Nov-23
St. Louis	Cortex-Tower Grove Connector - Signal Optimization-Tower Grv/Vandeventer: Laclede-Magnolia Cycle Track - Tower Grv/Vandventer: Magnolia-Sarah	7138-23	\$5,596,244	CONST	Jun-24
St. Louis	S. Broadway Cycle Track - Dover St To River City Casino Blvd Cycle Track (10') - Curb Ramps	7213-22	\$840,000	CONST	Jan-24
St. Louis	Tucker Boulevard Cycle Track - Washington Ave To Chouteau Ave (MO 100) Cycle Track (10') - Signal Updates - Bike Boxes - Ln Reconfig	7165-22	\$1,016,000	CONST	Jun-24
St. Louis County	Big Bend Road (East) - 2023 - Laclede Station Rd To E. Lockwood Ave Resurfacing - Curb Ramps	6963A-23	\$819,140	CONST	Jun-24

Not Obligated - Construction / Implementation					
Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
TOTAL			\$107,540,371	88 PROJECTS	
St. Louis County	Big Bend Road (West) - 2023 - Kirkwood Rd (US 61/67) To Couch Ave Resurfacing - Curb Ramps	6963B-23	\$1,145,880	CONST	Jun-24
St. Louis County	Craig Road - 2023 - Lackland Rd To Olive Blvd (MO 340) Resurfacing - Curb Ramps - Signals	6963C-23	\$1,340,160	CONST	Jun-24
St. Louis County	Ferguson Avenue - 2023 - St. Charles Rock Rd (MO 180) To Page Ave (MO D) Resurfacing - Curb Ramps	6963D-23	\$735,120	CONST	Jun-24
St. Louis County	Lackland Road - 2024 - Craig Rd To E/O Concourse Dr Resurfacing - Curb Ramps - Slab Replacement	7124A-22	\$1,047,520	CONST	Sep-24
St. Louis County	Mckelvey Road - 2023 - Natural Bridge Rd To I-270 Resurfacing - Curb Ramps	6963E-23	\$1,121,210	CONST	Jun-24
St. Louis County	Midland Blvd - 2023 - Page Ave (MO D) To Canton Ave Resurfacing - Curb Ramps	6963F-23	\$748,020	CONST	Jun-24
St. Louis County	N. Hanley Road (F) - 2024 - I-70 To Natural Bridge Rd (MO 115) Resurfacing - Curb Ramps	7124B-22	\$1,357,520	CONST	Sep-24
St. Louis County	New Florissant Road - 2023 - Lindbergh Blvd (US 67) To Washington St Resurfacing - Curb Ramps	6963G-23	\$1,185,140	CONST	Jun-24
St. Louis County	Old Jamestown Rd Sidewalk, Ph. 3 - Jamestown E.S. Entrance To Cedar Crest Creek Dr Sidewalk (5')	7167-22	\$597,890	CONST	Sep-24
St. Louis County	Olive Blvd - 2024 - Ferguson Ave To W/O Skinker Blvd (Stl City Limit) Resurfacing - Curb Ramps - Lane Reduction	7124C-22	\$892,880	CONST	Sep-24
St. Louis County	Paul & S. Elizabeth Ave - 2023 - Chambers To Bermuda Resurfacing - Curb Ramps	6963H-23	\$784,980	CONST	Jun-24
St. Louis County	Reavis Barracks Road/Green Park Road - Over Gravois Creek Replace Reavis Barracks Bridge - Realign Gp Rd To Reav. Barracks	7124G-22	\$5,560,100	CONST	Sep-24
St. Louis County	Redman Road - 2023 - Old Halls Ferry Rd To W/O MO 367 Resurfacing - Curb Ramps	6963I-23	\$1,210,990	CONST	Jun-24
St. Louis County	Sulphur Spring Road - 2024 - Manchester Rd (MO 100) To Big Bend Rd Resurfacing - Curb Ramps	7124D-22	\$1,105,100	CONST	Sep-24
St. Louis County	West Florissant Avenue - At Chambers Rd - Sidewalk (5') - Lighting Shared Use Path (8') - Intersection & Bus Stop Impr.	6963J-21	\$2,631,393	CONST	Jun-24
St. Louis County	West Florissant Avenue - 2024 - Lucas & Hunt To Solway Ave Resurfacing - Curb Ramps	7124E-22	\$1,371,040	CONST	Sep-24
St. Louis County	Woodson Road - 2024 - Brown Rd To Kempland Pl Resurfacing - Curb Ramps - Bike Ln	7124F-22	\$819,440	CONST	Sep-24
St. Peters	Mexico Road Bridge - At Dardenne Creek Bridge Rehabilitation	7197C-23	\$394,771	CONST	Dec-23
St. Peters	Mid Rivers Mall Dr - At St. Peters-Howell Rd Turn Lanes - Upgrade Traffic Signal	7212-22	\$364,192	CONST	Dec-23
Union	Union Expressway - MO 47/US 50 To MO 47/Old Country Farm Rd New Road	7125A-23	\$6,936,406	CONST	Jun-24
University City	Canton Avenue, Phase 2 - Midland Blvd To Pennsylvania Ave Full Depth Reclamation - Upgrade Sidewalks (5-6')	7126-22	\$926,314	CONST	Oct-23
University City	Ferguson Avenue Sidewalks - Melrose Ave To Olive Blvd (MO 340) Sidewalks (5')	7283-24	\$552,414	CONST	May-24
Vinita Park	North & South Road/Midland Sidewalks, Phase 2 - North & South: Page To Midland; Midland: North & South To Delpport Sidewalks (5-6')	6752A-21	\$704,000	CONST	Jun-24
Washington	Jefferson Street - Fifth St To MO 100 Resurfacing - Sidewalk (5') - Curb & Gutter	6970-21	\$1,075,940	CONST	Jun-24

Not Obligated - Construction / Implementation

Sponsor	Title - Description	TIP #	FY 2024	Phase	Scheduled Obligation
		TOTAL	\$107,540,371	88 PROJECTS	
Wentzville	Peine Road - 60' E/O Forest Way Dr To 675' W/O Stewart Springs Dr Resurfacing - Shoulders (3') - Curve Impr.	6972-21	\$1,013,773	CONST	Jun-24
Wentzville	Wentzville Parkway - Meyer Rd To Parkway Ridge Blvd Reconstruct - Twtl (Locally Funded) - Shared Use Path (10')	7127-23	\$1,117,478	CONST	Nov-23
Wentzville	Wentzville Parkway Sidewalk - W. Pearce Blvd To Veterans Memorial Pkwy Sidewalk (6')	7168-22	\$438,240	CONST	Jan-24
Wildwood	Manchester Road/Taylor Road - Manchester: MO 100-Old Fairway; Taylor: MO 100-Main St Resurfacing - Traffic Signal Upgrades - Optimization	7128-23	\$1,440,000	CONST	Jun-24
Wildwood	MO 109 - At MO BA (South) Roundabout - Shared Use Path (10')	7129-22	\$1,172,000	CONST	Nov-23
Wildwood	Old State Road Shared Use Path - Old State Place Dr To Nantucket Island Dr Shared Use Path (10') - Connection To Waterfront Way	7169-22	\$912,000	CONST	Dec-23

Bold Indicates Project Received One-Time Extension
